Technical Proposal

Client: **Hydra**

Project: **72xB300 proposal**

Document date: 2025-11-28

Table of contents

Table of contents 2

Executive summary 3

List of assumptions 4

Technical Solution description 5

Within the Scope of Ecoblox and its Partners 6

Out of scope 6

Offered solution for 72xB300 systems 7

Itemized component list 8

Design layout 11

Scope of Services 13

Financial details 14

Terms and conditions 15

Executive summary

This technical proposal details Ecoblox's comprehensive solution for customer's requirement to deploy 72xB300 HGX systems. Ecoblox's response to this challenge encompasses the design and delivery of a Tier 2 Modular Data Center (MDC) with integrated IT and power infrastructure specifically engineered to house the B300 systems alongside essential network management and general-purpose racks. The services provided extend to the complete installation and commissioning of the MDC, including advanced cooling and fire suppression systems, along with the physical rack & stack of IT equipment, comprehensive network cabling, and full project management for Ecoblox scope of work. The document further outlines the specific components and provides a financial overview. Key exclusions from the scope include the procurement and configuration of IT equipment and all necessary site preparation and civil construction.

List of assumptions

- No storage requirements

Technical Solution description

In this proposal Ecoblox is offering a design of 2 combined 40FT MDCs as one data hall designed to host 20 x 65kW RDHx racks capable of hosting the 72xB300 systems, network management, and general-purpose racks, and additional 40FT power room alongside cooling system solution.

Key components of the offered solution include:

- **Tier 2 MDC:** A combined 2x 40FT containers for IT, featuring a raised floor to support the 20x65kW RDHx racks.
- **Power Infrastructure:** Tier 2 level power container with PDMs, 1x 400V 3P 1500kVA UPS with N+1 hot-swap modules, 5-minute backup VRLA Battery system, ATS, and 40 metered PDUs.
- **Cooling System:** CDU and 4x 500kW Free Cool Chillers (outdoor equipment).
- **Monitoring & Security:** Integrated 21" display for internal monitoring of temperature, humidity, smoke, door status, and power voltage via SNMP. Includes security door access control and video cameras for room-level surveillance.
- **Fire Suppression:** Room-level gas type fire suppression system with Honeywell early detection alarm.

Ecoblox's scope of services encompasses the installation and commissioning of the MDC, cooling system, and fire suppression system, as well as the installation of IT equipment (rack & stack) and network cabling. Project management services for Ecoblox scope of work are also included, covering planning, risk management, communication, and reporting.

Out of scope items include the procurement and configuration of IT equipment (B300 systems, network equipment), and site preparation/civil construction work (foundations, MDC placement, power connections, generators, ATS, internet connectivity, and site physical security).

Within the Scope of Ecoblox and its Partners

Installation of MDC on site:

- Installation & commissioning of cooling system
- Installation & commissioning of fire suppression system

IT Equipment installation:

- Rack & stack
- Network installation & cabling

Project Management

- Creating a detailed project plan
- Identifying dependencies and potential risk
- Monitoring and managing risks throughout the project lifecycle
- Providing leadership and support to the team
- Establish communication channels with stakeholders
- Regular reporting on project progress and status
- Establish the process for managing changes to the project scope and requirements

Out of scope

IT Equipment & Configuration:

- Procurement of B300 systems
- Procurement of network equipment (cables, network switches)
- Configuration of IT equipment

Site Preparation & Civil Construction:

- Preparation of foundations for MDC (Modular Data Center) and cooling equipment (chillers, pumps, water tank)
- Placement of MDC and cooling equipment in designated positions
- Low voltage power preparation
- Connection of MDC to the electricity grid
- Procurement and installation of generators

- Securing internet connectivity on site
- Procurement and installation of ATS (automatic transfer switch)
- Site physical security (fencing, broader CCTV access)

Scope boundaries are critical for clearly defining the work to be performed within a project or agreement. Consequently, any deliverable, task, feature, or functionality that is not specifically and unambiguously detailed and included within the defined scope of work will be explicitly understood and treated as being outside the boundaries of that scope. This principle ensures that all stakeholders have a shared understanding of what is included and, equally importantly, what is excluded, thereby mitigating potential misunderstandings, scope creep, and disputes over deliverables or responsibilities. This exclusion applies regardless of whether the item is related to the overall project objectives or could be perceived as a natural extension of the defined work; if it is not expressly mentioned within the scope statement, it is considered out of scope..

Offered solution for 72xB300 systems

Itemized component list

Category	Item	Description	Qty
2x 40FT MDC as IT room	40Ft Data Center Container	Single Data Center Container, 12192(L) * 3600(H) * 3200(W)mm, including doors, cable management, LED lights kit, front and rear aisles, Anti-static raised floor and insulation walls. Integrated DCIM system with 10" display monitoring temperature&humidity, smoke, door and power, cooling. SNMP module for high level DCIM integration; Security 3 in 1(Pin/RFID/Fingerprint) access control, with video Camera and remote web/SMS/email; Room-level Gas type Fire suppression with Honeywell early detection alarm.	2
	Smart PDU Monitoring Type 24 IEC Sockets	Rated input three phase,current 63A, 3-bit C13 output socket, 21-bit C19 output socket with indicator, with total meter (hot-swapped IP-2017 digital current meter), 19-inch rack-type installation, with SNMP protocol, web view, with 3 meter cables and industrial socket.	40
	Wall Mount a/c 30kW w/ Heat & Hum	30kW wall mount type with inverter compressor, w/ reheater & hum, EC fan, packaged type with condenser built in, 380-415V/3P/50-60Hz. Power Type IEC 24kW, Unit width 1200mm	3
	600mm Rack	48U cabinet, including door, top & bottom panels, 9-folded frame, wheels and stand-levels, 600mm(width)*1200mm(depth)*2275mm(height), Vertical cable organizer with cable plate and tie points. Horizontal cable organizer including cable slot, fingers	20

		and cover, 1U height. Typical customer logo included.	
	65kW RDHX	Rear door heat exchanger CW type, 65kW cooling only, 2Way valve, carel controller. Power Type IEC 5.2kW	20
	Water Distribution Piping for RDHX	Underfloor water distribution piping system.	1
	PDC Floor Mount	Power distribution panel, including power input, power meters, surge protection, and power distribution&management braches of UPS, Cooling, UPS manual bypass, PDU, and surge protection. 600mm（W）*1200（D）* 2200mm（H）, 500kW	2
Power room	40Ft Power Room Container	Combined 2 standard 40ft container, 40Ft(L) * 9.5Ft(H) * 3300mm(W), including doors, cable management, LED lights kit, front and rear aisles, etc. and certificate for ocean shipment. Security 3 in 1(Pin/RFID/Fingerprint) access control, with video Camera; Room-level Gas type Fire suppression with Honeywell early detection alarm.	1
	1500kVA UPS & Battery system rack mount	400V3P 1500kVA UPS, with 12PCS 125kVA power modules, power efficiency >96%, 1600mm(W)* 1100mm（D）*42U Floor mount. VRLA battery, 432pcs 12V/260AH with Battery connection kit, and Confluence Box. In 6x racks, footprint 6x2850mm(W)*920mm(D)	1
	Wall Mount a/c 30kW w/ Heat & Hum	30kW wall mount type with inverter compressor, w/ reheater & hum, EC fan, packaged type with condenser built in, 380-415V/3P/50-60Hz. Power Type IEC 24kW, Unit width 1200mm	4
Outdoor equipment	Chiller 500kW	500kW chiller with free cooling eco mode. 6200mm（L）*2235mm（W）*2500mm（H）, Power 240kW(peak value), weight 8800 kg	4

	Chilled Water Pump CDU	CDU system for chilled water distribution, with water manifold and water shut-off valve. For cooling 500kW~1MW. Outside N+1 pump station 2050mm（L）*2660mm（W）*2100mm（H）, Power 30kW 3P 380-415V, weight 2120 kg	1
Warranty	Product Warranty	1 year warranty of product, covering components for replacement or repair. Not including all components/parts shipping cost. Customer shall cover all the labor costs for product recovery, service and maintenance.	1

**Subject to change upon completion and confirmation of the final design.*

Design layout

The following diagrams illustrate the proposed physical architecture for the 72xB300 systems deployment within the Ecoblox Modular Data Center solution.

Figure 1:Modular Data Center Footprint

This diagram depicts the integrated layout of the two 40FT containers on-site combined into one big data hall. It illustrates the arrangement of the 20x 600mm racks, specifically highlighting the placement of the 65kW Rear Door Heat Exchangers (RDHx).

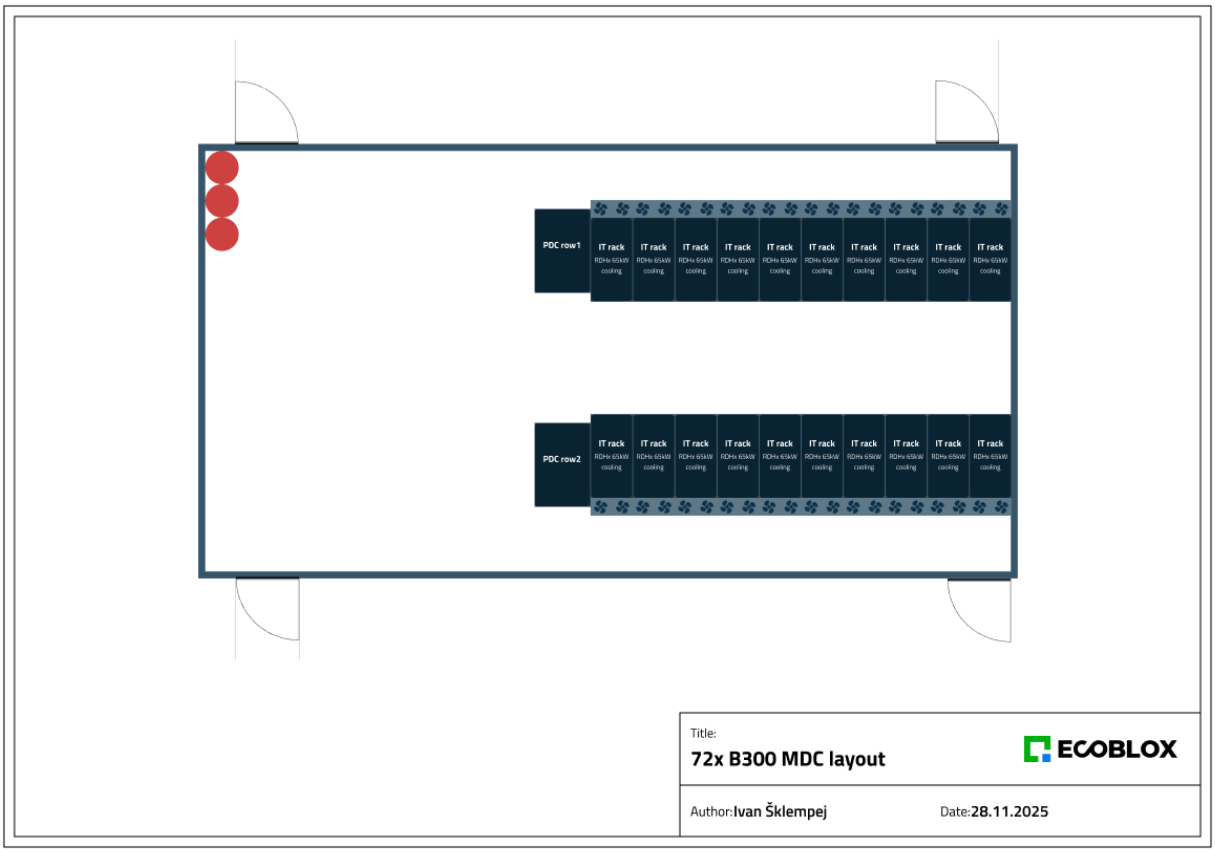

Figure 2: Power room configuration

This detailed view focuses on the interior of the power room.

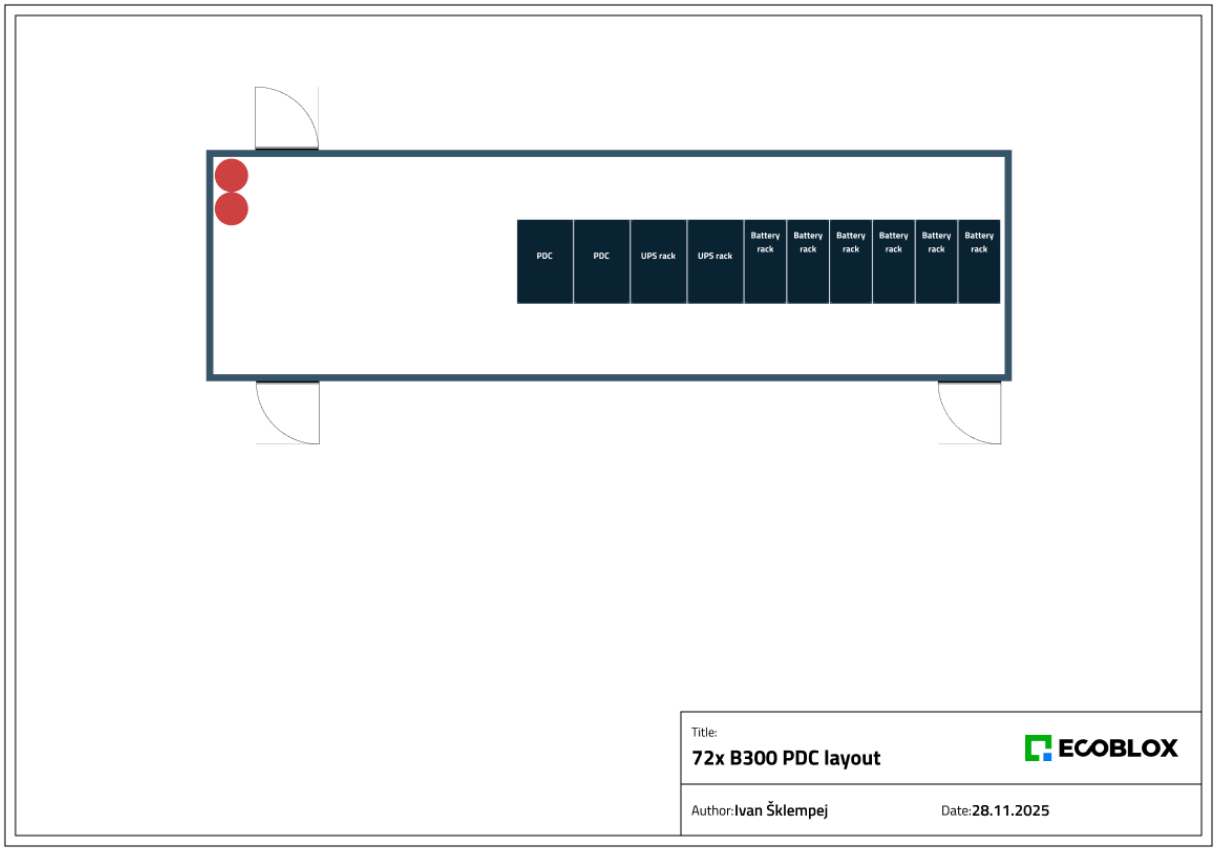

Scope of Services

Category	Item	Description	Qty
Ecoblox services	Installation & commissioning of MDC	Procurement, installation & commissioning of cooling system (vales, pipes, water tank)	1
		Fire suppression system installation & commissioning	
	IT equipment installation	Rack & stack	
		Network equipment installation	
		Networking & Cabling	
	Project Management	Creating a detailed project plan	
		Identifying dependencies and potential risk	
		Monitoring and managing risks throughout the project lifecycle	
		Establish communication channels with stakeholders	
		Regular reporting on project progress and status	

Financial details

Per deployment phase:

Category	Qty	USD
Tier 2 MDC for hosting 72xB300 systems	1	$2,816,757.79
Ecoblox services	1	$985,865.23
	Total:	**$3,802,623.02**

- 1-year warranty
- MDC Leadtime: 14 weeks from confirmed PO to pre-balance (can be reduced if higher prepayments are made)
- Payment term: T/T 40% upon PO, 60% prior shipment.
- Product cost only, not including Shipping delivery cost, Customs clearance cost, and any Tariff/Tax etc.
- Shall not be liable for any failure of or delay due to force majeure, such as natural disaster, war and country policy etc.
- Travel and accommodation expenses are not included in this proposal and will be invoiced separately

Terms and conditions

TBD
